Dependencies Diagram

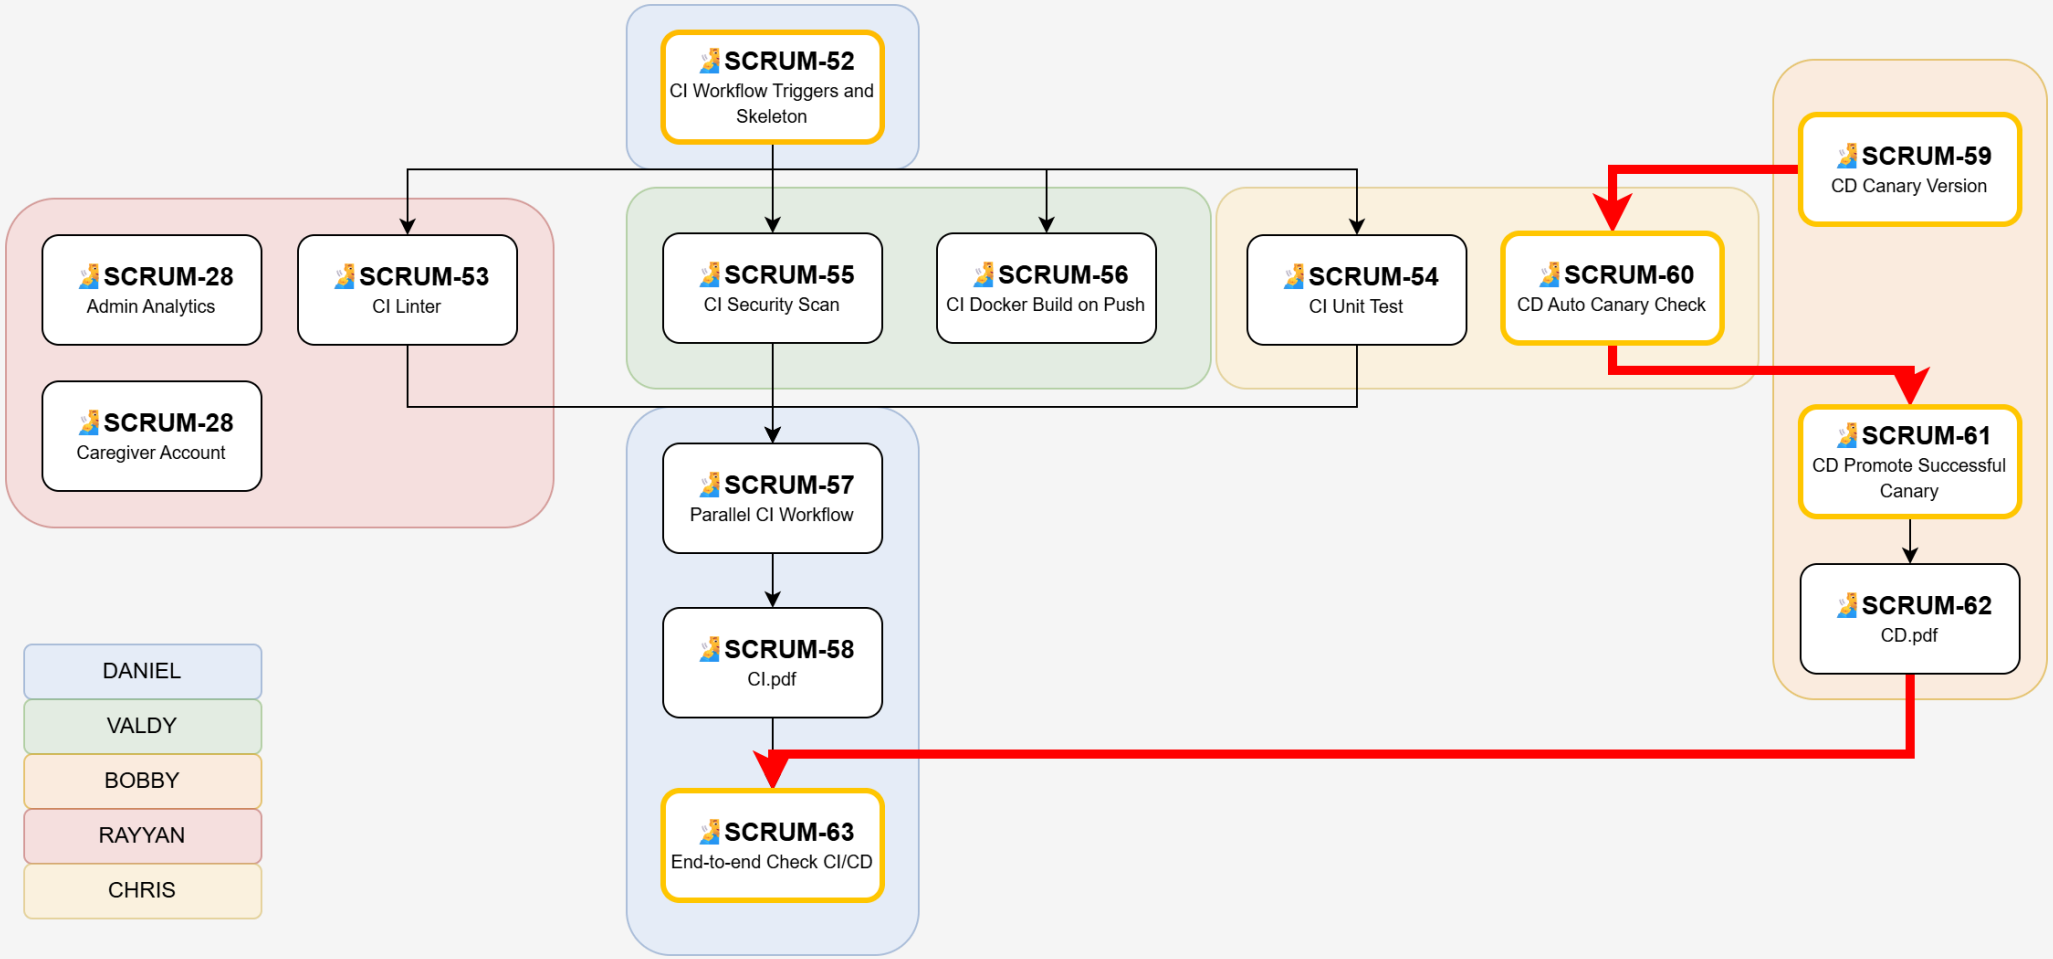

Critical Path

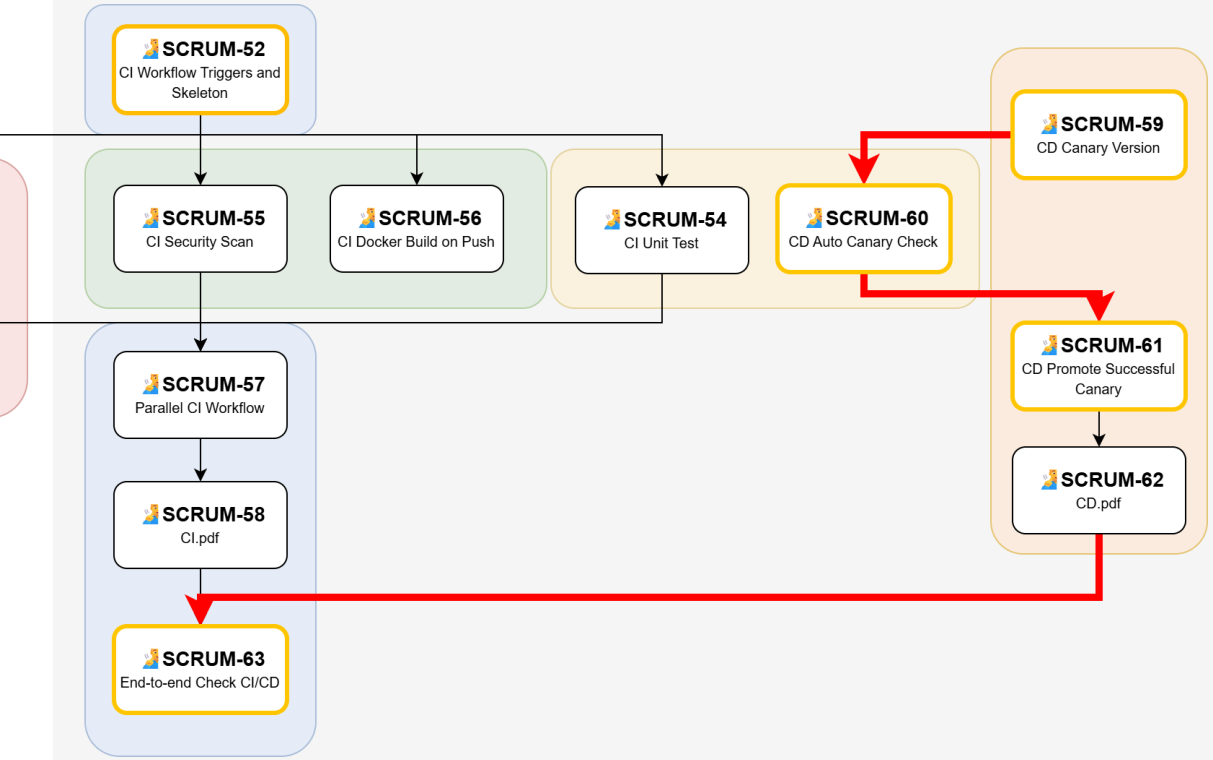

SCRUM-59, SCRUM-60, SCRUM-61, SCRUM-62, SCRUM-63

The main target for Sprint 4 is to finish the CI/CD pipelines. We made 59-60-61-62-63 (CD pipeline as the critical path) instead of the CI pipeline because building CI pipeline is easier for us to do as we already have experience in Docker, we also have made our unit tests, and multiple library exists to check code quality, and security scan.

Risk Area

SCRUM-52	SCRUM-59, 60, 61	SCRUM-63
This is a risk area as four other stories depend on this story as this story creates the skeleton (template) for other stories to start with.	This feature may have higher technical difficulties as it may require us to learn and study new technologies. Hence, the assignee have to spend more time on learning and researching what's best.	This area is the end-to-end check for CI/CD pipeline. Any error or mistake in the pipelines can cause the story to be long as it requires the assignee to fix those errors either by his own or by other's help.

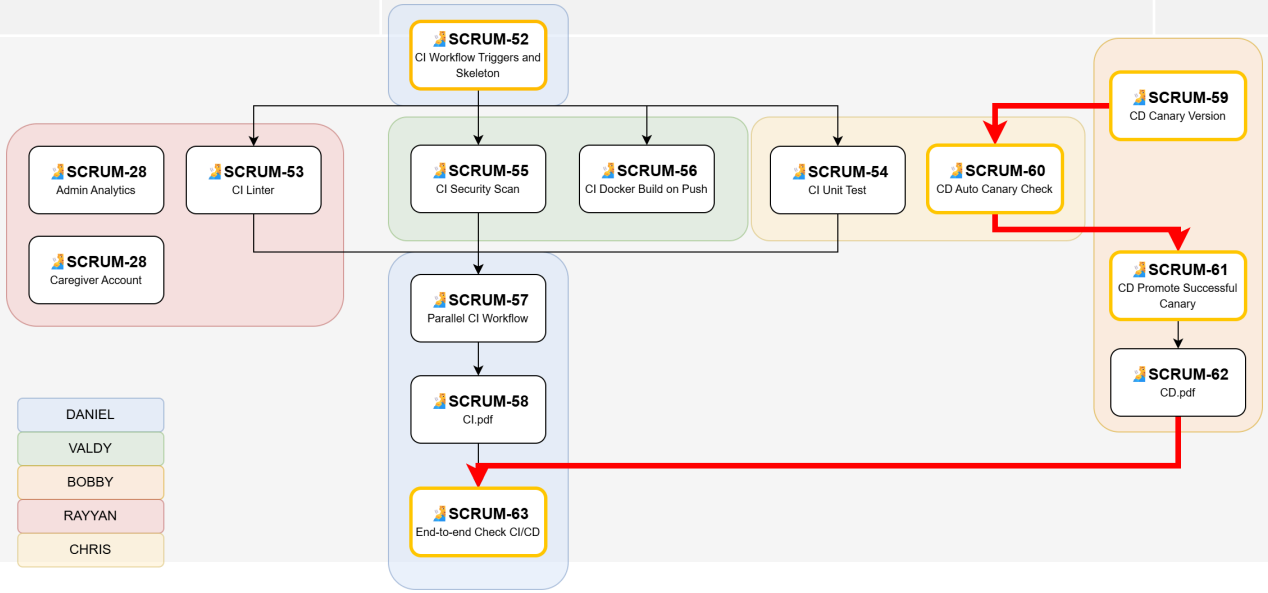

Lesson (and What Went Wrong?)

Speed or Equal Contributions?

Notice that in the CD pipeline stories diagram, Chris is assigned to SCRUM-60, while Bobby is assigned to the other CD pipeline-related stories.

With these assignments, it would be more efficient for Bobby to handle the entire CD pipeline, since having one person complete the whole pipeline would save time.

However, we made this assignment because we also wanted to ensure that everyone contributes equally to the project. Without SCRUM-60, Chris would only have one user story left to work on.

One advantage of this arrangement is that we now have two people working on the CD pipeline, allowing them to review and discuss the technical aspects more thoroughly
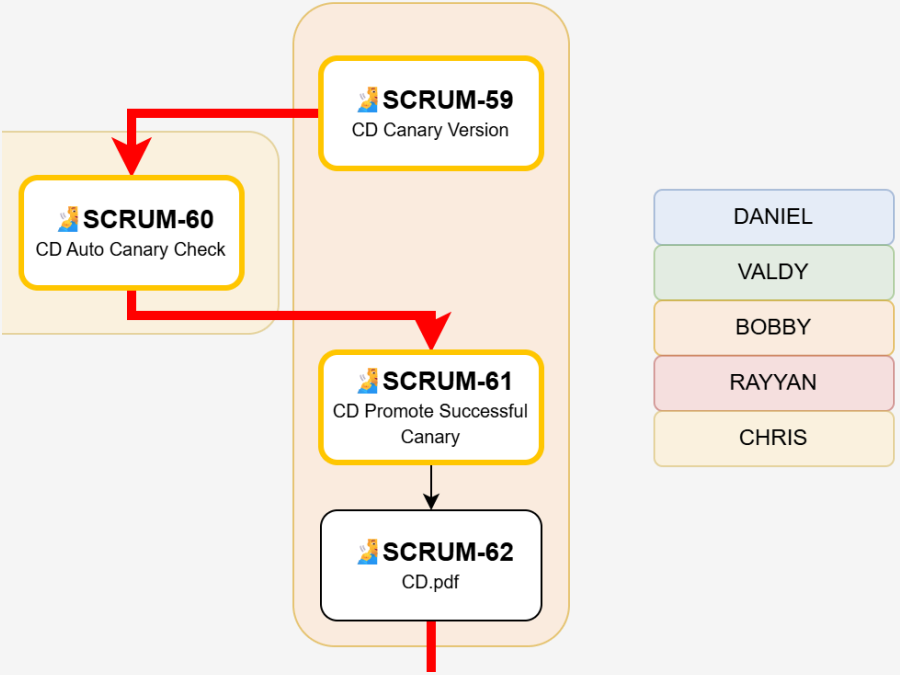
Since we have enough time and less stories to do this sprint, this approach is reasonable.
